



WEATHERFORD  
PUBLIC SCHOOLS  
EAST & WEST ELEMENTARY



September

9/30/2020

MONTHLY PROGRESS REPORT

## MONTHLY OVERVIEW

### WEST ELEMENTARY

- ◆ FINISHED POURING ALL THE FLOORS FOR THE SCHOOL
- ◆ CONTINUED WITH THE STRUCTURAL STEEL ERECTION
- ◆ STARTED ELECTRICAL ROUGH –IN OF THE MAIN ELECTRICAL FEEDS
- ◆ STARTED FRAMING EXTERIOR STUD WALLS
- ◆ STARTED POURING CONCRETE ON ALTERNATE DRIVE
- ◆ STARTED RUNNING WATER AND SEWER AROUND BUILDING

### EAST ELEMENTARY

- ◆ FINISHED POURING ALL CONTINUOUS AND SPOT FOOTINGS
- ◆ FORMED FLOOR FOR SLAB ON GRADE POUR
- ◆ FORMED AND Poured MUSSIC ROOM SHELTER



# UPCOMING ACTIVITIES

## WEST ELEMENTARY

- ◆ FINISH STEEL ERECTION AND ROOF DECKING
- ◆ COUNTINUE WITH METAL STUD FRAMING
- ◆ CONTINUE WITH ELECTRICAL ROUOGH—IN
- ◆ INSTALL ROOF DRAINS
- ◆ INSTALL ROOF CURBS
- ◆ FORM AND POUR EAST RETAINING WALL

## EAST ELEMENTARY

- ◆ FINISH POURING SHELTERS
- ◆ PREP AND POUR FLOORS FOR BUILDING SLAB







# PHOTOS





PHOTOS

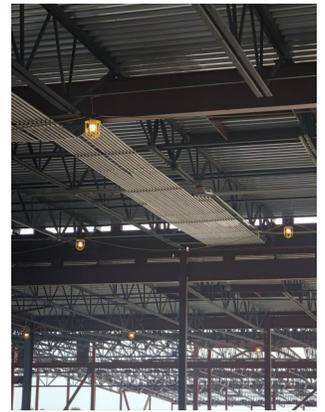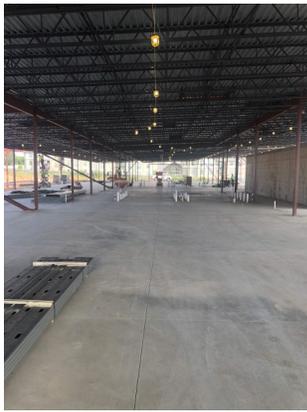



# PHOTOS



