



Community Meeting

Water Contract 1211

Ashburton Reservoir

Zone II Tanks

December 4, 2024 – 6:00 PM

Involved Neighborhoods:

- ✓ Ashburton
- ✓ Forest Park
- ✓ Hanlon – Longwood
- ✓ & Vicinity




What is the project status?

- Project Began: Spring 2018
- Days Used: 2,409 CCD
- Project Budget: \$136,964,200.00
- Work Completed: 94%
- Days Remaining: -468 CCD
- Contract Completion Date: 8/24/2023
- Functional Use Achieved: 12/7/2023




Project Completion Status

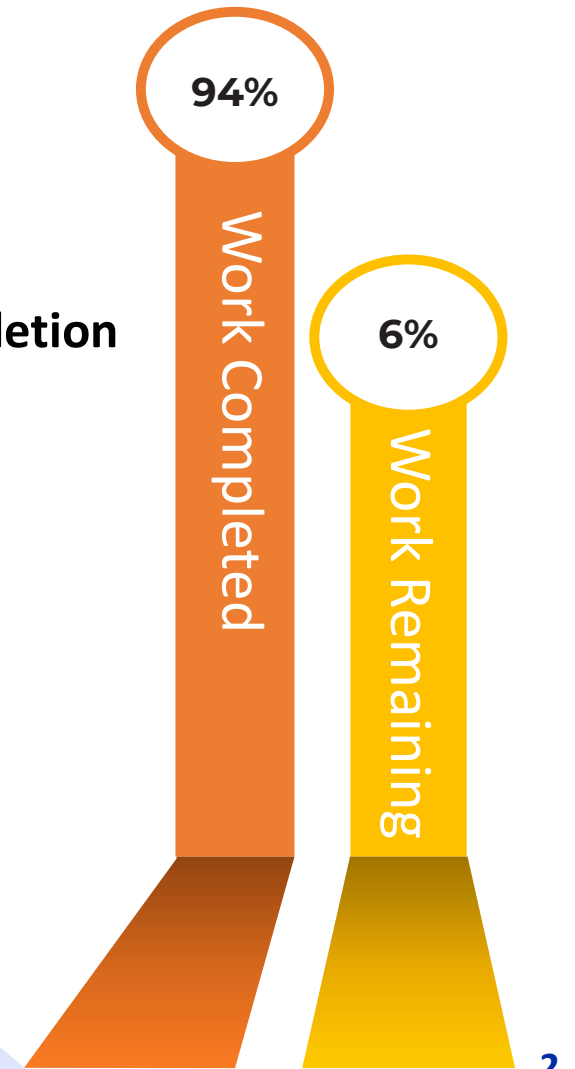

What is completed?

- Tank Excavation Completed
- Tank Construction Completed
- Water Distribution Piping
- Tanks & Associated Water Piping in Service

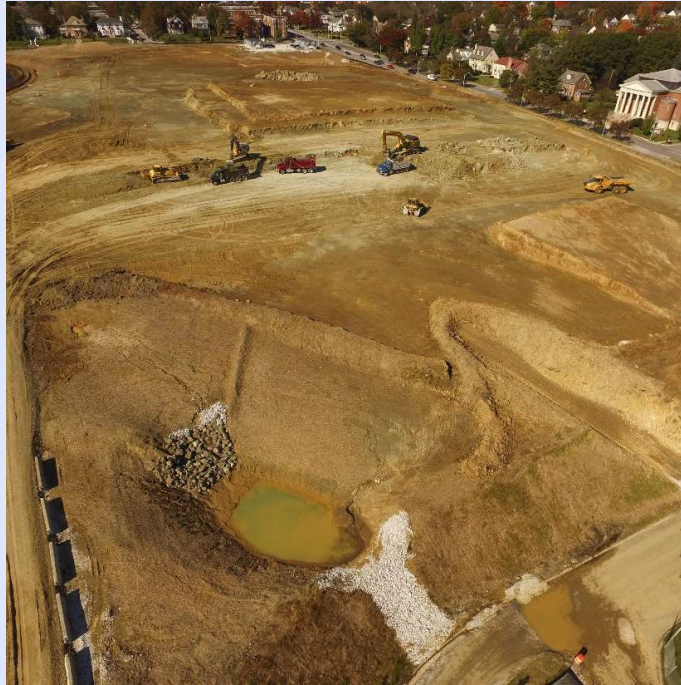

Mass excavation for the new Water Tanks and Distribution Building - 10/30/2018



Installation of Geomembrane on top of Tank A & Backfill of Tank B – 11/27/2024



What is happening?

- Commissioning of Distribution Building and Testing of Instrumentation & Control Systems
- Installation of Site Storm Water Piping
- Installation of Tanks Roof Drainage System
- Backfilling of the Tanks
- Installation of Tank Access Structures
- Installation of Pavilion, Playground, Comfort Station & Other Park Amenities



Installation of Pavilion & Playground – 11/27/2024



What is happening?

➤ Site Storm Water Piping Installation



Storm Water Piping Installation – 11/15/2024

➤ Backfill of Tanks



Backfill of Wing Walls – 11/27/2024



What are the next steps?

- Complete Processing of Stockpile
- Continue Backfilling of the Tanks & Roof Drainage System
- Continue Installation of Tank and Lake Overflow Piping
- Filling of the Lake
- Installation of Lake Aeration System
- Restoration of Park - Playground, Comfort Station, & Park Amenities



Site Construction – 11/27/2024





Project Area

- Due to construction activity, public access to the park will remain limited.
- Most of the entrance and exit for construction vehicles will be on Liberty Heights Avenue at Dukeland Street.





Community impacts?

- The sidewalk along the south side of Liberty Heights Avenue from Hilton St. to Dukeland St. continues to be closed.
- Public transportation is still accessible



What are the plans for public safety?

- We are taking necessary steps to ensure a safe construction site environment for everyone.
- Signage will clearly identify the construction area, and access will be restricted and closely monitored.
- Contractors will make every effort to reduce noise and maintain site.
- Dust sensors will be monitored and calibrated.





When is the next community meeting?

- Community meetings for the Ashburton Reservoir Zone II Tanks project will continue to be held quarterly
- Meetings will continue to be held virtually via MS Teams
- The next community meeting is scheduled for Wednesday, March 5, 2025 @ 6:00PM



How can I stay informed?

Contact Information

DPW Community Liaison:

Anthony Greene

Anthonyl.greene@baltimorecity.gov

(410) 274-5918

DPW/OEC Project Manager:

Charles Oliver

Charles.oliver@baltimorecity.gov

(443) 324-6530

