



Decommissioning
San Onofre
Nuclear Generating Station
Safety | Stewardship | Engagement

LEARN MORE ABOUT THE DECOMMISSIONING OF THE SAN ONOFRE NUCLEAR POWER PLANT.

COME

to the plant and take a walking tour. Scan this QR code to schedule your visit.



About Us

Decommissioning

Safety

VISIT

songscommunity.com for the most current information about our decommissioning activities and deconstruction schedule.

TALK TO US

We'd be happy to come share information about the plant with you, your community association or organization.

Decommissioning
San Onofre
Nuclear Generating Station
Safety | Stewardship | Engagement



SONGS – SCE
P.O. Box 4030
San Clemente, CA 92674

To contact our deconstruction liaison
call **1 (888) 797-2404** or email us at
SONGSdecomm@sce.com



Decommissioning
San Onofre
Nuclear Generating Station
Safety | Stewardship | Engagement

SAN ONOFRE DECOMMISSIONING UPDATE

**Q4
2025**

As December ended, so did the fifth full year of decommissioning activities at SONGS. With the dedication and focus of site personnel, work continues to be performed safely and efficiently. Since the first truck and rail car left the site, just over 630 million pounds of waste and debris have been removed.

Here is our annual look back at our progress in 2025 by the numbers and for the overall project:

- We have now removed 48 structures from the site
- Almost 231.5 million pounds of waste shipped offsite this year
- Approximately 870,000 pounds of decommissioning materials were recycled for a project total of 108 million pounds to date
- 1,179 rail cars transported waste and materials offsite in 2025 with a project total of 2,558 rail cars
- 65 tours hosted over 1,200 visitors witnessing our progress throughout 2025

In 2026, we continue demolition onsite and will begin dismantlement of the Unit 3 containment dome.




First to go - The area inside and around the Unit 3 containment dome is being cleared in preparation for dismantlement later this year.




DECONSTRUCTION ACTIVITY

All deconstruction activity will take place at the SONGS site

Schedule is subject to change. In addition to the activities listed below, material deliveries and waste shipments will continue throughout the deconstruction period.

LEGEND	WORK ACTIVITY	WORK PERFORMED Q4 2025	WORK AHEAD Q1 2026
	North and East areas (parking lot areas)	<ul style="list-style-type: none"> Continued material delivery and removal Began removal of equipment from Parking Lot 4 	<ul style="list-style-type: none"> Continue material delivery and removal Continue equipment removal from Parking Lot 4
	Containment Buildings (Units 2 & 3 domes) and connected buildings	<ul style="list-style-type: none"> Completed demolition of connected buildings Completed removal of Units 2 & 3 large components Continued Unit 3 hazardous material removal Completed Unit 2 Tank Building demolition Completed Unit 3 reactor segmentation Began construction of Unit 3 Material Handling Tent 	<ul style="list-style-type: none"> Continue Unit 2 demolition of connected buildings Begin Unit 2 reactor segmentation Begin Unit 2 Material Handling Tent (MHT) construction Continue Unit 3 hazardous materials removal Begin Unit 3 interior demolition Complete Unit 3 Material Handling Tent construction
	Outer Buildings (administration buildings)	<ul style="list-style-type: none"> Continued to manage material and load railcars 	<ul style="list-style-type: none"> Continue to manage material and load railcars
	Turbine Building and Intake/Forebay Structure	<ul style="list-style-type: none"> Continued demolition material management 	<ul style="list-style-type: none"> Continue demolition material management
	South Yard Buildings	<ul style="list-style-type: none"> Began cleanout and waste packaging 	<ul style="list-style-type: none"> Continue cleanout and waste packaging Begin isolation of utilities
Site wide		<ul style="list-style-type: none"> Continued site assessments and monitoring Continued waste shipments 	<ul style="list-style-type: none"> Continue site assessments and monitoring Continue waste shipments

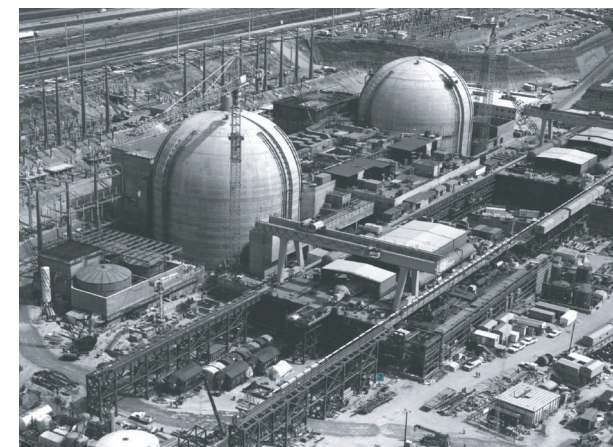

Stages of construction and destruction: A look at SONGS during start-up construction in late 1970's versus recent demolition progress from 2025.
