

WEEKLY REPORT



CATALYST

Project Name : St. Pauls Onalaska

Full Address : 1201 Main St. Onalaska 54650

Date : 1/11/24

Project Photos

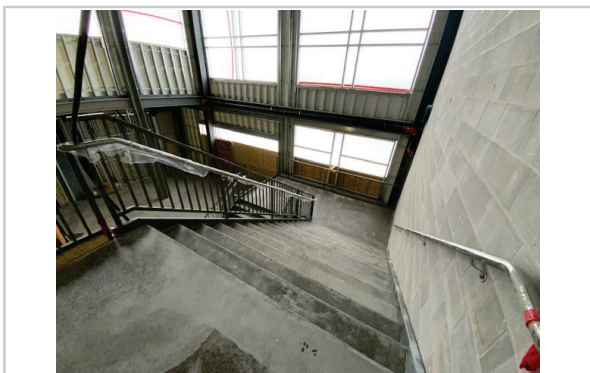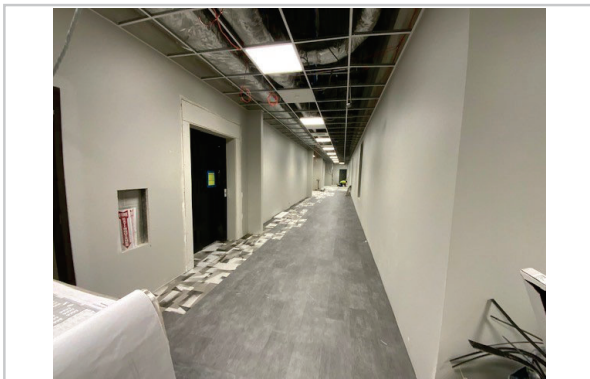

Construction Activities

Weeks Activities

Exterior Lobby Steel Studding Complete
Interior Lobby Studding
Pour Lobby stair pans
Bath partitions
Casework and tops
Ceramic tile and grout Locker area
Painting door frames
Data wiring
Electrical Contractor continues sub panel feeds
Plumbing Contractor continues water lines and Mech. Room water piping including water meter.
Ceiling grid 1st and 2nd floors
Install full tiles 2nd floor
Drywall hanging continues
Begin North canopy framing
LVT flooring 1st and 2nd floor

WEEKLY REPORT

CATALYST



Complete the form below

Project Name : St. Pauls Onalaska

Full Address : 1201 Main St. Onalaska 54650

Date : 1/11/24

Project Photos



Upcoming Activities

Complete Commons Stage decking
 Interior lobby steel studding
 Flooring Wall Base
 Mechanical Finishes
 Casework
 Data wiring
 Painting stair 123
 Drywall finishes
 Lobby Mechanical in wall roughs
 Measure for Lobby exterior panels
 Permanent heat to gym , upper
 classrooms
