

PROJECT UPDATE

Issue No. 12
August 2022

Balmorhea New Campus




Area 'E' Metal Stud Framing - 07.20.2022



Area 'C' Slab & Metal Stud Layout - 07.20.2022



Aerial Looking Northwest - 07.22.2022

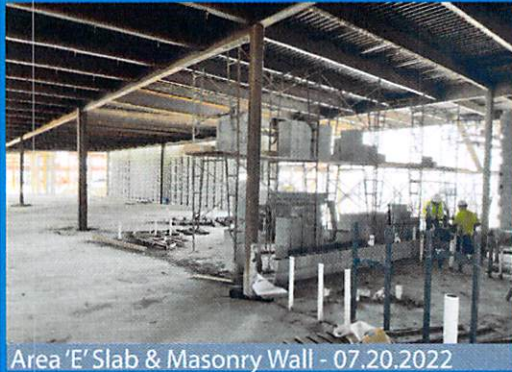

Area 'E' Slab & Masonry Wall - 07.20.2022



Area 'C' Deck & Metal Studs - 07.13.2022



Track & Field, Track Installation - 07.13.2022

Progress to Date


- Completed track surface installation.
- Completed structural steel erection in Area A & B.
- Completed high roof metal stud install at Area E2.
- Completed concrete slab pours in Areas C & E.
- Continued plumbing and electrical underground rough-ins at Areas A, B, & D.
- Continued concrete block installation in Area E.
- Continued HVAC duct layout/hanger installation in Area C.
- Continued concrete slab reinforcing stl. assembly.
- Continued metal deck installation in Areas A & B.
- Began sprinkler pipe mains installation.
- Began interior metal stud layout.
- Began utility yard and transformer pad installation.
- Began stadium ticket booth foundations.

Looking Ahead

- Complete dirtwork; rework erosion caused by rain runoff.
- Complete Area D underground plumb./elect.
- Complete concrete slab pour in Area D.
- Complete miscellaneous steel installation.
- Continue metal deck and metal stud installation.
- Continue concrete slab reinforcing stl. assembly in Areas A & B.
- Continue concrete slab pour in Area D.
- Begin HVAC duct installation.
- Begin conc. sidewalks.

2019 Bond Project

- GMP Money Authorized to Date
- Completion of Project
- Schedule for Project

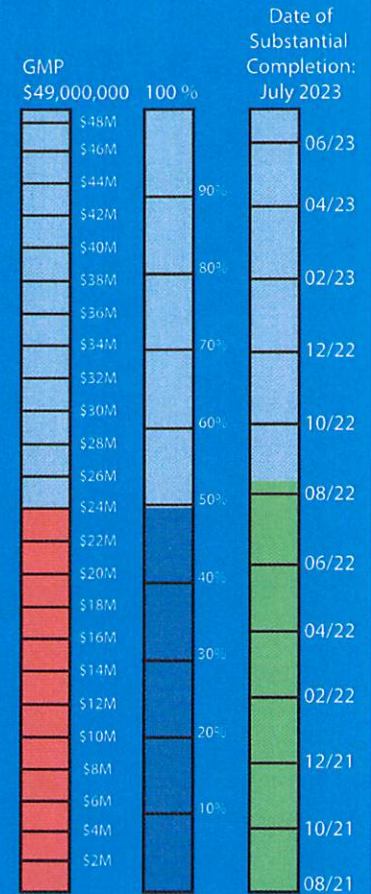

BALMORHEA

