

PROJECT UPDATE

Issue No. 05
January 2022


Balmorhea New Campus



Overall Aerial _ 01.07.2022



Offsite Utilities Excavation and Replacement Upgrades _ 01.07.2022

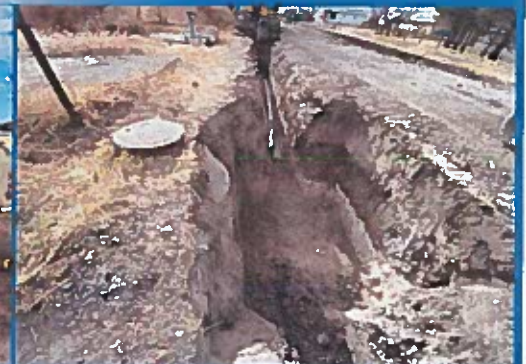

Area E Footprint _ 01.07.2022



Poured Foundation Footing _ 12.08.2021



Foundation Reinforcing Steel _ 12.08.2021

Progress to Date


- Site dirtwork is 80% complete.
- Completed offsite sanitary sewer trenching and installation along Third Street.
- Completed onsite sanitary sewer line mains.
- Continued excavation of main detention pond;
- Continued processing/distribution of detention pond soil on site.
- Continued foundation rebar and setting concrete forms in E1/E2.
- Continued 3" gas line installation from Railroad down along San Angelo and onto meter location.
- Began football stadium layout of track & field; contractor is establishing work point.
- Received delivery of bentonite clay for gym.
- Received first trucks of structural steel.

Looking Ahead

- Complete E1/E2 foundation/grade beams.
- Continue dirtwork.
- Continue football stadium track & field layout.
- Continue installation of sanitary sewer laterals.
- Begin E1/E2 underground plumb./elect.
- Begin Area C foundation excavation.
- Begin termite control spraying at gym.
- Begin formwork installation for curbs at field.
- Begin bentonite clay installation.

2019 Bond Project

- GMP Money Authorized to Date
- Completion of Project
- Schedule for Project

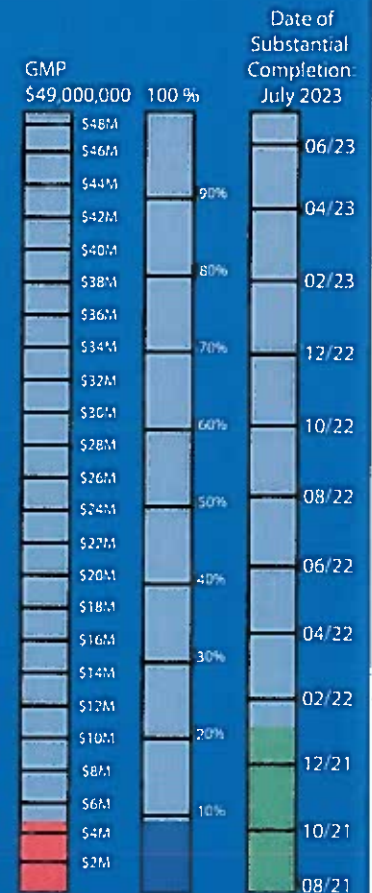

BALMORHEA

CLAYCOMB
ASSOCIATES ARCHITECTS
