


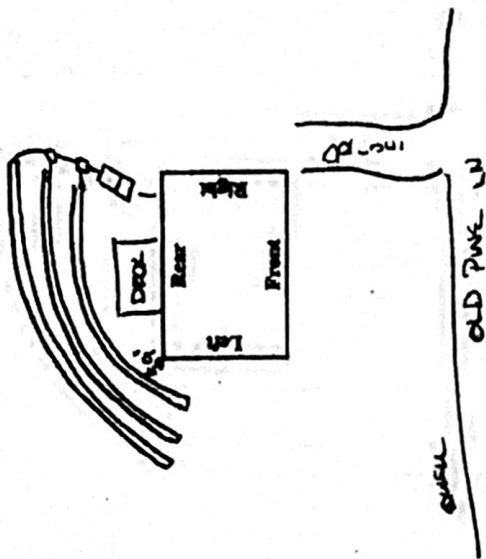

HOUSE SEWER: 7 feet from right, left, front, rear corner.

SEPTIC TANK: Front, rear, right side, left side of building. Perpendicular, parallel, angle 10 feet from building.

DISTRIBUTION BOX: 3 feet from end side, corner of septic tank.

NITRIFICATION FIELD OR FILTER: 9' feet from building at nearest point.

WELL (IF ANY): 100' feet from septic tank and 100' feet from disposal field.

SOIL APPEARANCE: Suitable, Provisionally suitable

REMARKS:

GASTON COUNTY SEPTIC TANK INSPECTION RECORD
ENVIRONMENTAL HEALTH DIVISION

sewer system #

DATE: 9/2/04

CODE/SUB EAST FIELD

SCANNED:

Owner Name: STARK, HAROLD
 Address: 5012 OLD PLANK LN.
 City/ST.: CHERK/VILLE, NC
 Zip: 28621
 Prev. Owner:
 Receipt #: 33574
 Date Installed: 9/2/04
 Improve. Permit #: 21059
 Type Dwelling: SFD (HOUSE)
 No. of Bedrooms: 3
 # Users/Tot. People: 6
 Garbage Disposal: N (V/N)
 Basement: N
 Plumbing: N (V/N)
 Est. Daily Flow: 360

No. of Tanks: 1
 No. of Tanks: 1
 Cap: 1000
 Type Sewer System: MTS
 Description: 1000 SFD
 Sub. Name: EAST FIELD
 Loc/Subdiv.: 5012 OLD PLANK LN.
 Type Well: C Lot # 13 Block #
 Lot Area: 30,000 Ft.
 Contractor: KRAUSE/KRUSE
 Precast Contractor: BELL NCS
 Max. Depth: 36"
 Width: 300
 Un. Ft.: 300
 Sq. Ft.: 900
 [Repair] # Trenches:
 Sq. Ft.:
 Un. Ft.:
 Width:
 Max. Depth:
 Sep. Trench/Wash:
 Sq. Ft.:
 Un. Ft.:
 Width:
 Max. Depth:
 Depth of Stone:
 Tax Book #: 2
 Code #: 2
 (A) Public Comm. (B) Public Non-Comm. (C) Ptv. (D) Comm. (E) Municipal
 Inspected By: JASON M. CONRAD

LEE PAGE
